

	<b>(B)</b>	Name	Duration	Start	Finish	Predecessors
1		Solution Planning	49 days?	11/1/17 8:00 AM	1/8/18 5:00 PM	
2	Ö	High Level Solution Planning	49 days?	11/1/17 8:00 AM	1/8/18 5:00 PM	
3		Requirements Specifications	19 days?	11/1/17 8:00 AM	11/27/17 5:00 PM	
4	Ö	High Level Solution Design	31 days?	11/27/17 8:00 AM	1/8/18 5:00 PM	
5		End of Solution Planning	0 days	1/8/18 5:00 PM	1/8/18 5:00 PM	2;3;4
6	Ö	Test Management	15 days	1/10/18 8:00 AM	1/30/18 5:00 PM	
7		Test Cases Identification	5 days	1/10/18 8:00 AM	1/16/18 5:00 PM	5
8		Test Cases Documentation	10 days	1/17/18 8:00 AM	1/30/18 5:00 PM	7
9		End of Test Management	0 days	1/30/18 5:00 PM	1/30/18 5:00 PM	8
10	Ö	Implementation	51 days?	1/31/18 8:00 AM	4/11/18 5:00 PM	9
11		Module: Content Repository	14 days?	1/31/18 8:00 AM	2/19/18 5:00 PM	
12		Revisit Analysis	1 day	1/31/18 8:00 AM	1/31/18 5:00 PM	9
13		Revisit Design	1 day	2/1/18 8:00 AM	2/1/18 5:00 PM	12
14		Identification of Content Repository	3 days	1/31/18 8:00 AM	2/2/18 5:00 PM	9
15		Create Baseline Container	5 days	2/5/18 8:00 AM	2/9/18 5:00 PM	14
16		Installation and Configuration	5 days	2/12/18 8:00 AM	2/16/18 5:00 PM	15
17		Unit Testing	1 day	2/19/18 8:00 AM	2/19/18 5:00 PM	16
18		Milestone#1: Content Repository Esta	0 days?	2/19/18 5:00 PM	2/19/18 5:00 PM	17
19		Module: Content Scrapping Module	14 days	2/20/18 8:00 AM	3/9/18 5:00 PM	
20		Revisit Analysis	1 day	2/20/18 8:00 AM	2/20/18 5:00 PM	18
21		Revisit Design	1 day	2/20/18 8:00 AM	2/20/18 5:00 PM	18
22		Write Scrapping utility for dawn.com	5 days	2/20/18 8:00 AM	2/26/18 5:00 PM	18
23		Write Scrapping utility for tribune.com	5 days	2/27/18 8:00 AM	3/5/18 5:00 PM	22
24		Write code to interlink news	3 days	3/6/18 8:00 AM	3/8/18 5:00 PM	23
25		Unit test	1 day	3/9/18 8:00 AM	3/9/18 5:00 PM	24
26		Milestone#2: Content Scrapping Finis	0 days	3/9/18 5:00 PM	3/9/18 5:00 PM	25
27		Module: API Gateway	7 days	3/12/18 8:00 AM	3/20/18 5:00 PM	
28		Revisit Analysis	1 day	3/12/18 8:00 AM	3/12/18 5:00 PM	26
29		Revisit Design	1 day	3/12/18 8:00 AM	3/12/18 5:00 PM	26
30		Identification of solution stack	3 days	3/12/18 8:00 AM	3/14/18 5:00 PM	26
31		Development of APIs	4 days	3/15/18 8:00 AM	3/20/18 5:00 PM	30
32		Milestone#3: API gateway completion	0 days	3/20/18 5:00 PM	3/20/18 5:00 PM	31
33		Module: Mobile App for Displaying	16 days	3/21/18 8:00 AM	4/11/18 5:00 PM	
34		Revisit Analysis	1 day	3/21/18 8:00 AM	3/21/18 5:00 PM	31
		Revisit Design	1 day	3/21/18 8:00 AM	3/21/18 5:00 PM	31

Resource Names	29 Oct	17	5 N	lov 17		12	Nov 17		19	Nov 17 M T W T	2	6 Nov	17	3	Dec 17	.1_ 1_	10	Dec 17		17 Dec
	S M T	W T  F	S  S	M T  W	T  F	S  S	M  T  W T	[  F	S S	M T WT	F  S  S	S  M  T	W T  F	-  S  S	M T W	/ T  F	S  S	M T W	T  F  S	S  S  M  T
												_								
							Cont	ent A	agren	gator - page	e2									

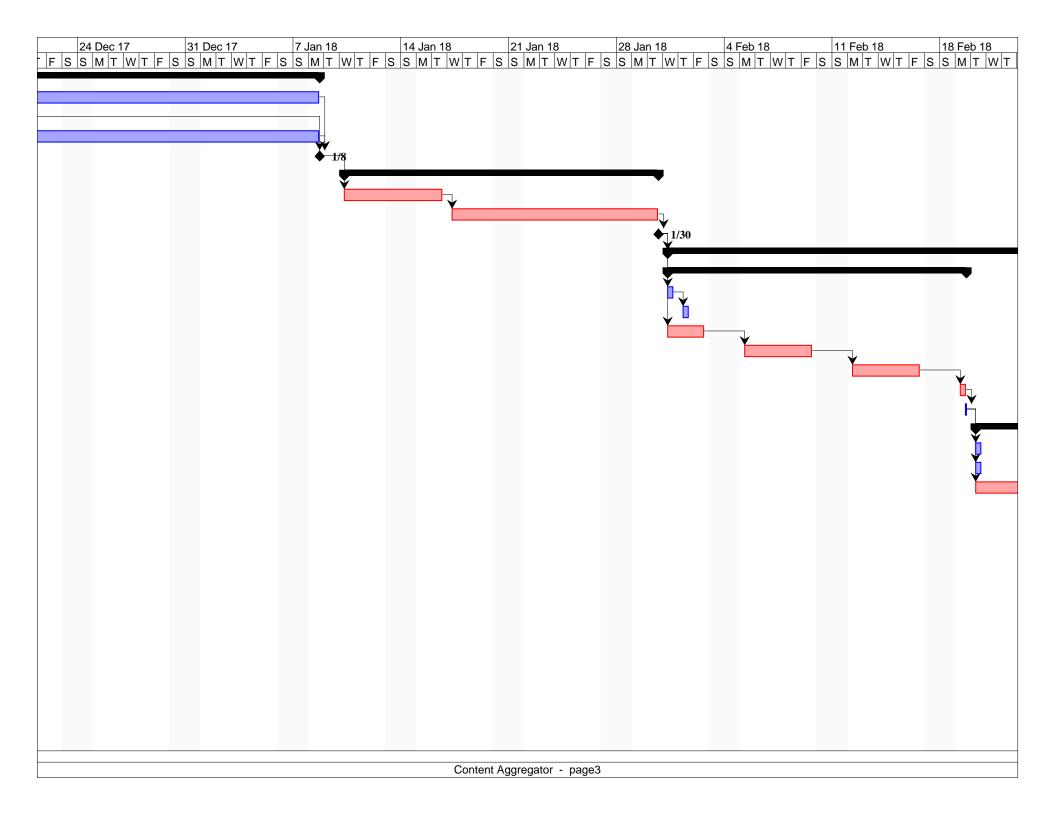


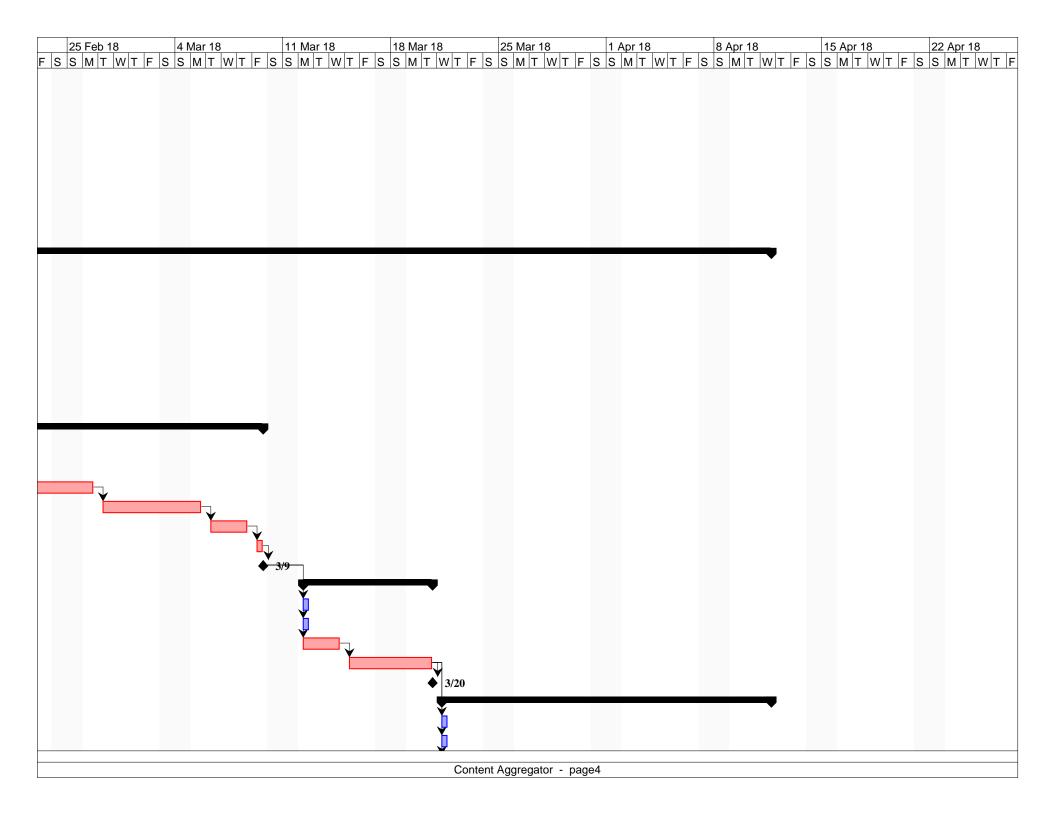


	29	Αp	r 1	8		F		61	May	/ 18	3		
S	S	М	Т	W	Т	F	S	S	M	Т	W	Т	F
		Cc	nte	ent	Ag	gre	gat	or	- p	age	e5		

	<b>(B)</b>	Name	Duration	Start	Finish	Predecessors
36		Development / Coding	15 days	3/21/18 8:00 AM	4/10/18 5:00 PM	31
37		Unit Test	1 day	4/11/18 8:00 AM	4/11/18 5:00 PM	36
38		Milestone#4: Mobile App completion	0 days	4/11/18 5:00 PM	4/11/18 5:00 PM	37

Resource Names	29 Oct	17	5 N	Nov 17		12	Nov 17		19	Nov 17		26	Nov 1	7	3	Dec 17		10	Dec 17	,	17	Dec 17 M T W 1
110500106 Hallies	SM	T WT F	SS	M T W	T F S	ss	M T W	Γ F	s s	M T W	/ T  F	s s	МТ	W T F	sss	MT	W T  F	s s	MT	W T  F	s s	M T W T
							Cont	ent A	aarea	ator - p	age7											

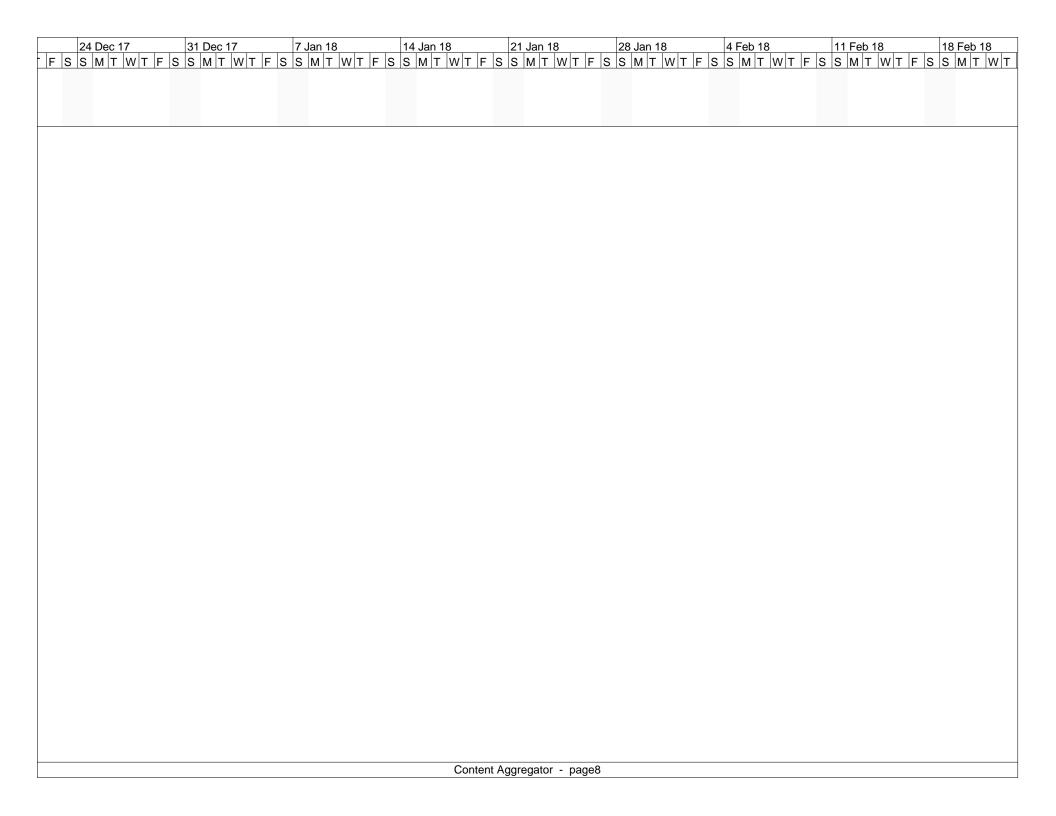

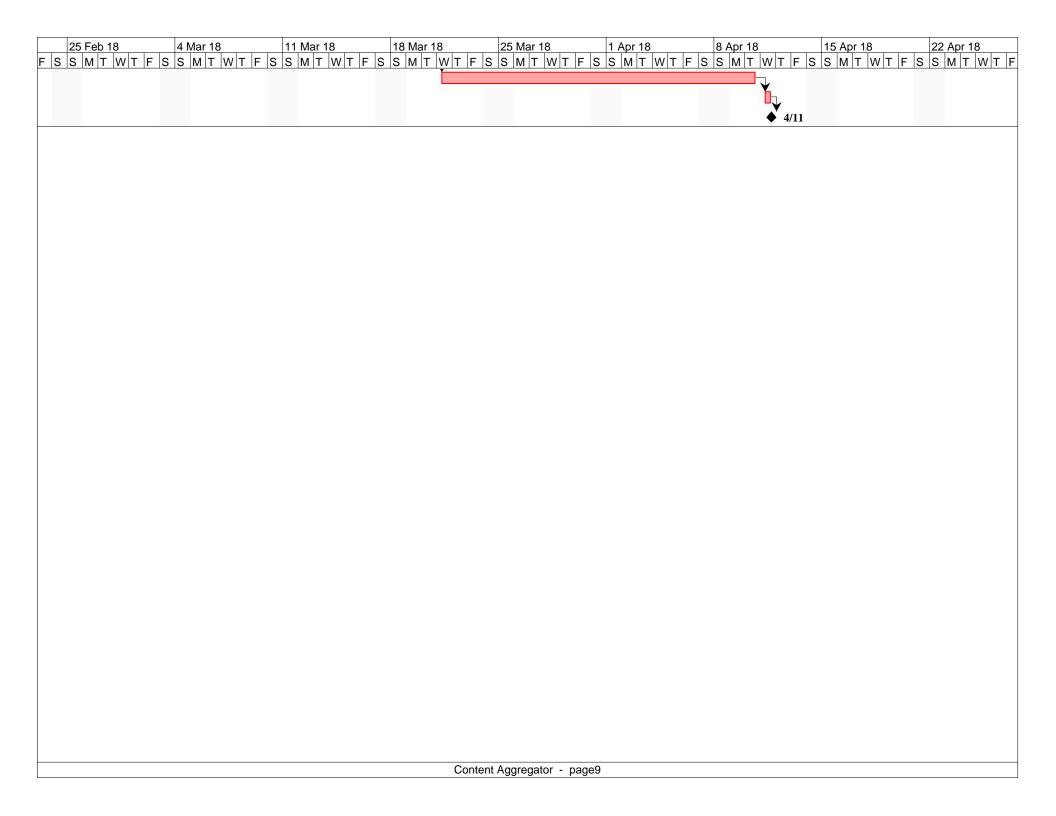

_	29	Αp	<u>r 1</u>	8		6 May 18 S M T W T F									
S	S	М	Т	8 W	Т	F	S	S	М	Т	W	Т	F		
		C 0.	nto	nt /	\ aa	iror	nato	\r	n	200	10				
		CU	ıııe	nt /	·yς	i e (	jail	л <b>-</b>	ρċ	age	10				
